



STATEMENT OF WORK

Wedding & Corporate Event Planning Platform

PREPARED BY

ArtWorksIT

PROJECT COMPLETION

Mid-November 2026

PROJECT START

31 August 2026

PROJECT TIMELINE

10 to 11 weeks

Project Objective

ArtWorksIT proposes to design and develop Phase One of a web-based event planning and vendor management platform for ConnectX.

The proposed platform will allow users to create and plan events, define individual sub-events, discover and select vendors, facilitate enquiries and negotiations, and track the progress of their event through a centralised interface.

The initial phase is intended to establish the core planning and marketplace infrastructure while keeping the system flexible enough to support future enhancements, including deeper operational workflows, hybrid or offline service models, and AI-assisted functionality.

The platform is proposed to support both wedding and corporate events. While the underlying planning flow will remain similar, the experience can accommodate the different requirements and contexts of each event type.


CO-FOUNDERS

Prranit Bhanne and Mukesh Tekchandani

Project Scope & Timelines

A key objective will be to ensure that the platform is not approached simply as a marketplace for venues or individual vendors. The proposed experience will instead begin functioning as an event planning platform from Phase One.

PROPOSED PROJECT START 31st August 2026	PROPOSED PROJECT COMPLETION Mid-November 2026	PROJECT TIMELINE Approximately 10 to 11 weeks
--	--	--

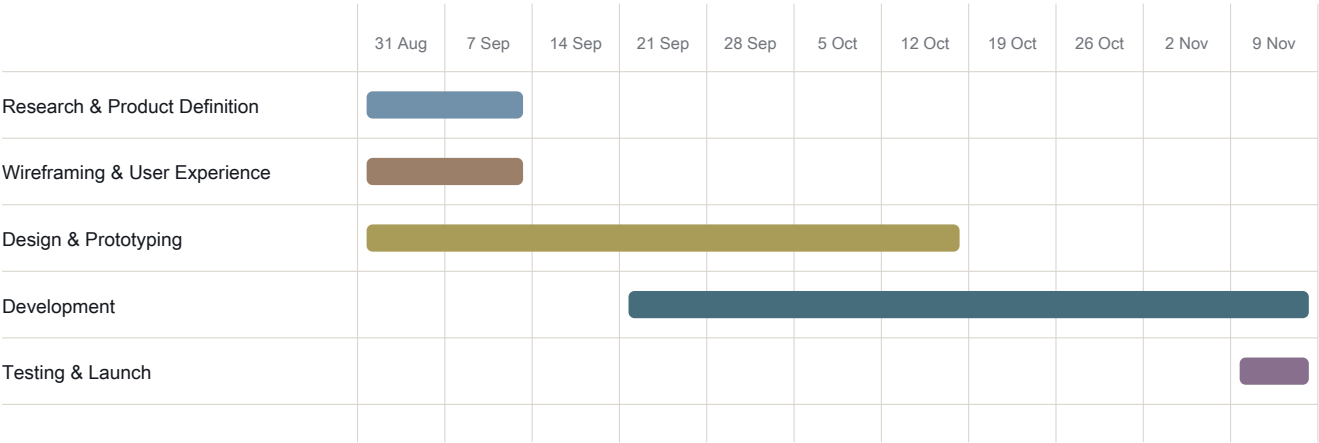

Parallel tracks indicate where project stages overlap.

Research & Product Definition

2 weeks

We will begin by understanding the complete system, its users, dependencies and the actions that may need to take place across the platform, both within Phase One and in future iterations.

The research phase will establish the core product structure and identify the information, fields, workflows and dependencies required across customers, vendors and the ConnectX administration team.

A key objective will be to ensure that the platform is not approached simply as a marketplace for venues or individual vendors. The proposed experience will instead begin functioning as an event planning platform from Phase One, helping users understand what needs to happen, what has been planned, what has been booked and what remains to be completed.

DELIVERABLE

Product structure, functional mapping and low-fidelity product direction.

31 AUG – 13 SEP 2026

Wireframing & User Experience

Included within the initial product definition and wireframing phase

Based on the research, we will map the primary user journeys and translate the proposed product structure into low-fidelity wireframes.

This stage will define the key screens, data points, fields, navigation and control flows across the customer, vendor and administrative interfaces.

The experience will account for event creation, sub-events, vendor discovery, vendor selection, proposals, negotiations, notifications and event progress. We will also define how users can visualise the overall state of their event and understand the completion of key planning activities.

The wireframes will also help establish how the platform can evolve beyond the initial implementation without requiring the underlying product structure to be rebuilt.

DELIVERABLE

Wireframes and user-flow definitions.

Design & Prototyping

A little over one month

Once the product structure and wireframes have been established, we will develop the visual language and interface design for the platform.

This will include typography, layout, interface components, graphics, visual hierarchy and interaction patterns. Particular attention will be given to making a data-heavy application understandable and accessible, with information presented in a way that allows users to quickly understand what is happening within their event.

The primary usage environment is expected to be desktop, while the interface will also be designed responsively for mobile devices. Mobile layouts will focus on condensing event information and navigation without compromising usability.

The designs will be presented to the Client for review and feedback. Once the design direction is sufficiently defined, the relevant screens will be frozen for development.

DELIVERABLE

High-fidelity interface designs and interactive prototypes.

Development

Runs progressively through the development period

Development will begin progressively alongside the product definition and design process rather than only after the visual design stage is complete.

Because the proposed platform is backend and workflow heavy, the underlying systems, dashboards, vendor structures, proposal mechanisms, communications and supporting workflows will begin taking shape from the early stages of the project.

Once the interface design is established, front-end development will proceed alongside the backend implementation.

Development will focus on responsive behaviour, data-heavy interfaces, interaction patterns and the practical usability of the platform across its different user types.

DELIVERABLE

Functional web application on staging environment.

Testing & Launch

Included within the overall project timeline

The completed platform will be tested across its core workflows and relevant devices before launch. A staging environment will be used for review and User Acceptance Testing.

Following completion of testing and agreed fixes, the platform will be prepared for production deployment and launch.

DELIVERABLE	Tested production-ready web application.
-------------	--

UAT

The project includes up to 2 consolidated rounds of UAT feedback and fixes during the staging phase. Bugs are limited to deviations from the approved designs or agreed functionality. New features, enhancements or changes in scope will be treated separately.

Core Platform Scope

Event Creation & Planning

Users will be able to create an event and define its primary details, including event dates and the individual sub-events that form part of the overall occasion.

- Wedding events and their individual functions or ceremonies.
- Corporate events and destination-oriented event requirements.
- Separate planning flows for individual sub-events.
- A central view of the overall event and its planning status.

Vendor Discovery & Selection

The proposed platform will allow users to discover and select vendors across relevant event categories such as venues, photography, decoration, SFX, choreography and other event services.

Vendor recommendations may be surfaced based on requirements such as budget, location, style and other relevant event preferences.

Vendor Profiles

The platform will provide profiles for vendors and customers, creating a structured interface through which relevant information can be presented and interactions can take place.

Proposals & Negotiation

Phase One will facilitate vendor enquiries, proposals and negotiation through the platform. Financial transactions are proposed to remain outside the system during this initial phase.

- Users can enquire with relevant vendors.
- Vendors can respond with proposals.
- The platform can facilitate proposal and negotiation workflows.
- Key status changes can be surfaced to the relevant users.

Event Progress & Completion

The proposed platform will provide users with a way to understand the progress of their event.

In the initial phase, completion can be represented through key planning actions such as finalising vendors for the relevant sub-events. This metric is intended to evolve as the platform develops and additional event-planning workflows are introduced.

Notifications & Communication

Users and vendors will receive relevant notifications when important events or workflow changes occur within the platform.

- Proposal and vendor communication updates.
- Key planning status changes.
- Important event-related notifications.
- Email and platform communication where applicable.

ConnectX Administration

An administrative interface will allow the ConnectX team to participate in and mediate relevant workflows between customers and vendors.

The administrative layer is intended to provide ConnectX with visibility and control over the platform while supporting the possibility of future hybrid and offline service models.

Phase One Boundaries

Phase One is proposed as the foundation of the ConnectX platform. The system will be structured with future expansion in mind. Any subsequent phase or additional functionality will be scoped and commercialised separately.

- 01 Financial transactions are proposed to remain outside the platform during Phase One. The platform will support vendor discovery, enquiries, proposals and negotiations, but will not process or accept payments from users in this phase.
- 02 Proposal and negotiation workflows are included within the initial platform concept.
- 03 Future hybrid or fully offline ConnectX-managed workflows can be supported through later phases.
- 04 AI-assisted functionality is reserved for a future phase and is not included in the current Phase One implementation.
- 05 Advanced operational workflows and additional automation can be scoped separately as the product evolves.

Technology & Product Considerations

- 01 01Responsive web application architecture
- 02 02Backend and database-driven workflows
- 03 03Customer, vendor and administrative interfaces
- 04 04Structured vendor and event data
- 05 05Notification and communication workflows
- 06 06Scalable architecture for future product enhancements

The proposed technology stack includes Laravel, Livewire, Alpine.js, TailwindCSS and GSAP. The front-end implementation may use additional supporting technologies where appropriate based on the requirements identified during development.

Pricing & Milestones

The total proposed price for Phase One of this project is INR 10,00,000 + GST.

The proposed payment structure consists of three milestones.

Milestone	Timeline	Payment
Initiation	31st August 2026	INR 3,30,000 (33%)
Design Sign-off	Design completion / mid-project	INR 3,30,000 (33%)
Project Go-live	Mid-November 2026	INR 3,40,000 (34%)

Support & Maintenance

- 01 The initial post-launch support period will cover bug fixes relating to the delivered Phase One functionality for one month after go-live.
- 02 A bug is understood as a deviation from the approved design or agreed functionality, rather than a new feature or enhancement.
- 03 New functionality, additional modules, significant workflow changes or enhancements requested after delivery will be scoped separately.
- 04 ArtWorksIT proposes to recommend, configure and manage the hosting infrastructure based on the platform's load, requirements and assets. The appropriate server environment will be assessed as part of the implementation.

Terms & Assumptions

Project Deliverables & Code Ownership

ArtWorksIT assures that all code and design components created for the Client's platform are original and tailored to the project's requirements. Code and documentation will be versioned and securely managed through GitHub, providing Client access to code versions and updates as needed. Upon full payment, the Client will have ownership of the custom website or application code, design files and project-specific deliverables created by ArtWorksIT, excluding third-party software, libraries, frameworks, fonts, plugins, stock assets and other components subject to their respective licences. ArtWorksIT reserves the right to showcase the completed project in its portfolio and marketing materials unless otherwise agreed upon in writing.

Confidentiality & Data Security

Both parties agree to keep all shared information confidential and will not disclose it to third parties without prior written consent. This provision will remain effective after the project's completion.

Client Responsibilities & Project Scope

The Client is responsible for providing all necessary project details, business rules, content, vendor information and timely feedback required for the project. The Client will provide timely access to relevant stakeholders for product decisions, approvals and clarification of workflows. Delays in requirements, content, approvals, feedback or other Client dependencies may result in corresponding changes to the project timeline.

Payment Terms & Financial Conditions

All payments are due Net 7 days from the invoice date, and all prices are exclusive of GST. The total project fee excludes costs for external services that may be required. Work will begin once the initial payment is received. If there are delays in payments, work may be paused temporarily and resumed once outstanding payments are cleared. The platform will be scheduled for go-live upon receipt of the applicable go-live stage payment.

Termination, Dispute Resolution & Governing Law

Either party may terminate the agreement in the event of a material breach by providing written notice. If terminated, Client agrees to compensate ArtWorksIT for services rendered and any applicable expenses. Disputes will first be addressed through good-faith negotiations. If unresolved, both parties consent to submit to the exclusive jurisdiction of the courts in Bangalore. This Agreement is governed by and construed under the laws of India, with Bangalore courts having exclusive jurisdiction.

Modifications & Entire Agreement

This document contains the full understanding between the parties and supersedes previous agreements. Any modifications must be in writing and signed by both parties.

Assumptions

The Client is responsible for providing the final requirements, business rules, content guidelines and necessary assets. Data entry and migration of extensive vendor or event data will be the responsibility of the Client unless specifically included in the scope. Hosting and infrastructure management will be defined as part of the final implementation and commercial arrangement. The platform will be developed in phases, and functionality not explicitly included in Phase One will be considered for subsequent phases.

STATEMENT OF WORK

Wedding & Corporate Event Planning Platform



ArtWorksIT
artworksit.com



PREPARED BY
Uday Rathore
+91 87927 45204
